UNC-Bingham Facility

WASTEWATER INFRASTRUCTURE IMPROVEMENTS PROJECT SCHEDULE

12/22/2010
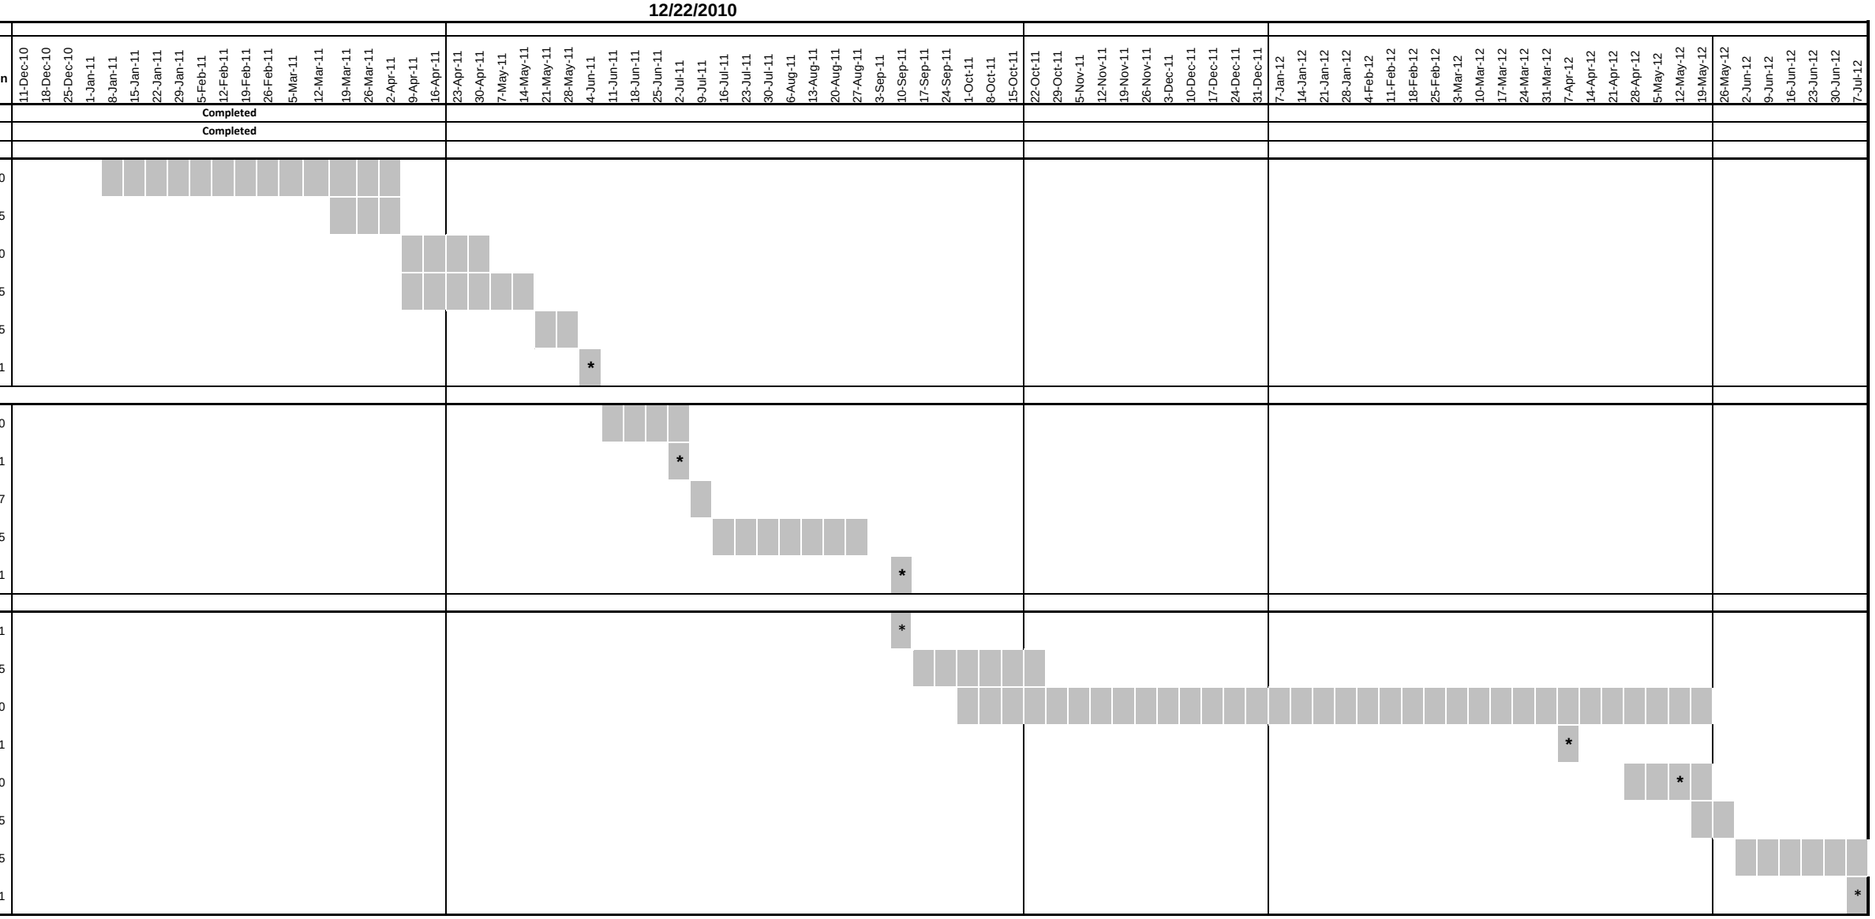
DESCRIPTION	Start Date	Finish Date	Task Duration
PHASE 1: ASSESSMENT ACTIVITIES			
PHASE 2: ALTERNATIVES ANALYSIS			
PHASE 3: DESIGN			
3.1 Construction Drawings	01/03/2011	04/03/2011	90
3.3 UNC Review	03/19/2011	04/03/2011	15
3.3 State Construction Construction Documents Review	04/03/2011	05/03/2011	30
3.4 NCDENR 2T Permit Modification Application	04/03/2011	05/18/2011	45
3.5 Revised Bid & Construction Documents	05/18/2011	06/02/2011	15
3.6 Authorization to Bid from SCO	06/02/2011	06/03/2011	1
PHASE 4: BID AND AWARD			
4.1 Bid Advertisement	06/08/2011	07/08/2011	30
4.2 Bid Opening	07/08/2011	07/08/2011	1
4.3 Recommendation for Award	07/08/2011	07/15/2011	7
4.4 Notice of Award	07/15/2011	08/29/2011	45
4.5 Notice to Proceed	09/13/2011	09/14/2011	1
PHASE 5: CONSTRUCTION			
5.1 Pre-Construction Meeting	09/14/2011	09/14/2011	1
5.2 Shop Drawing Submittals	09/13/2011	10/28/2011	45
5.3 Construction	09/27/2011	05/24/2012	240
5.4 Substantial Completion	04/24/2012	04/24/2012	1
5.5 Final Completion	04/24/2012	05/24/2012	30
5.6 Startup & Commissioning	05/24/2012	05/29/2012	5
5.7 Decommissioning Animal Wastewater Systems	05/29/2012	07/13/2012	45
5.8 Engineer's Final Certification	07/14/2012	07/14/2012	1
